


Duneland School Corporation Long-Term Capital Improvements Projects

Board Update

March 6, 2023



Duneland School Corporation Long-Term Capital Improvement Projects

Board Update March 6, 2023



Table of Contents

Westchester Intermediate

- Project Key Plan
- Progress Photos and Update

Yost (NEW) Elementary


- Project Key Plan
- Progress Photos and Update

Liberty Intermediate

- Project Key Plan
- Progress Photos and Update



Westchester Intermediate/Middle Key Plan

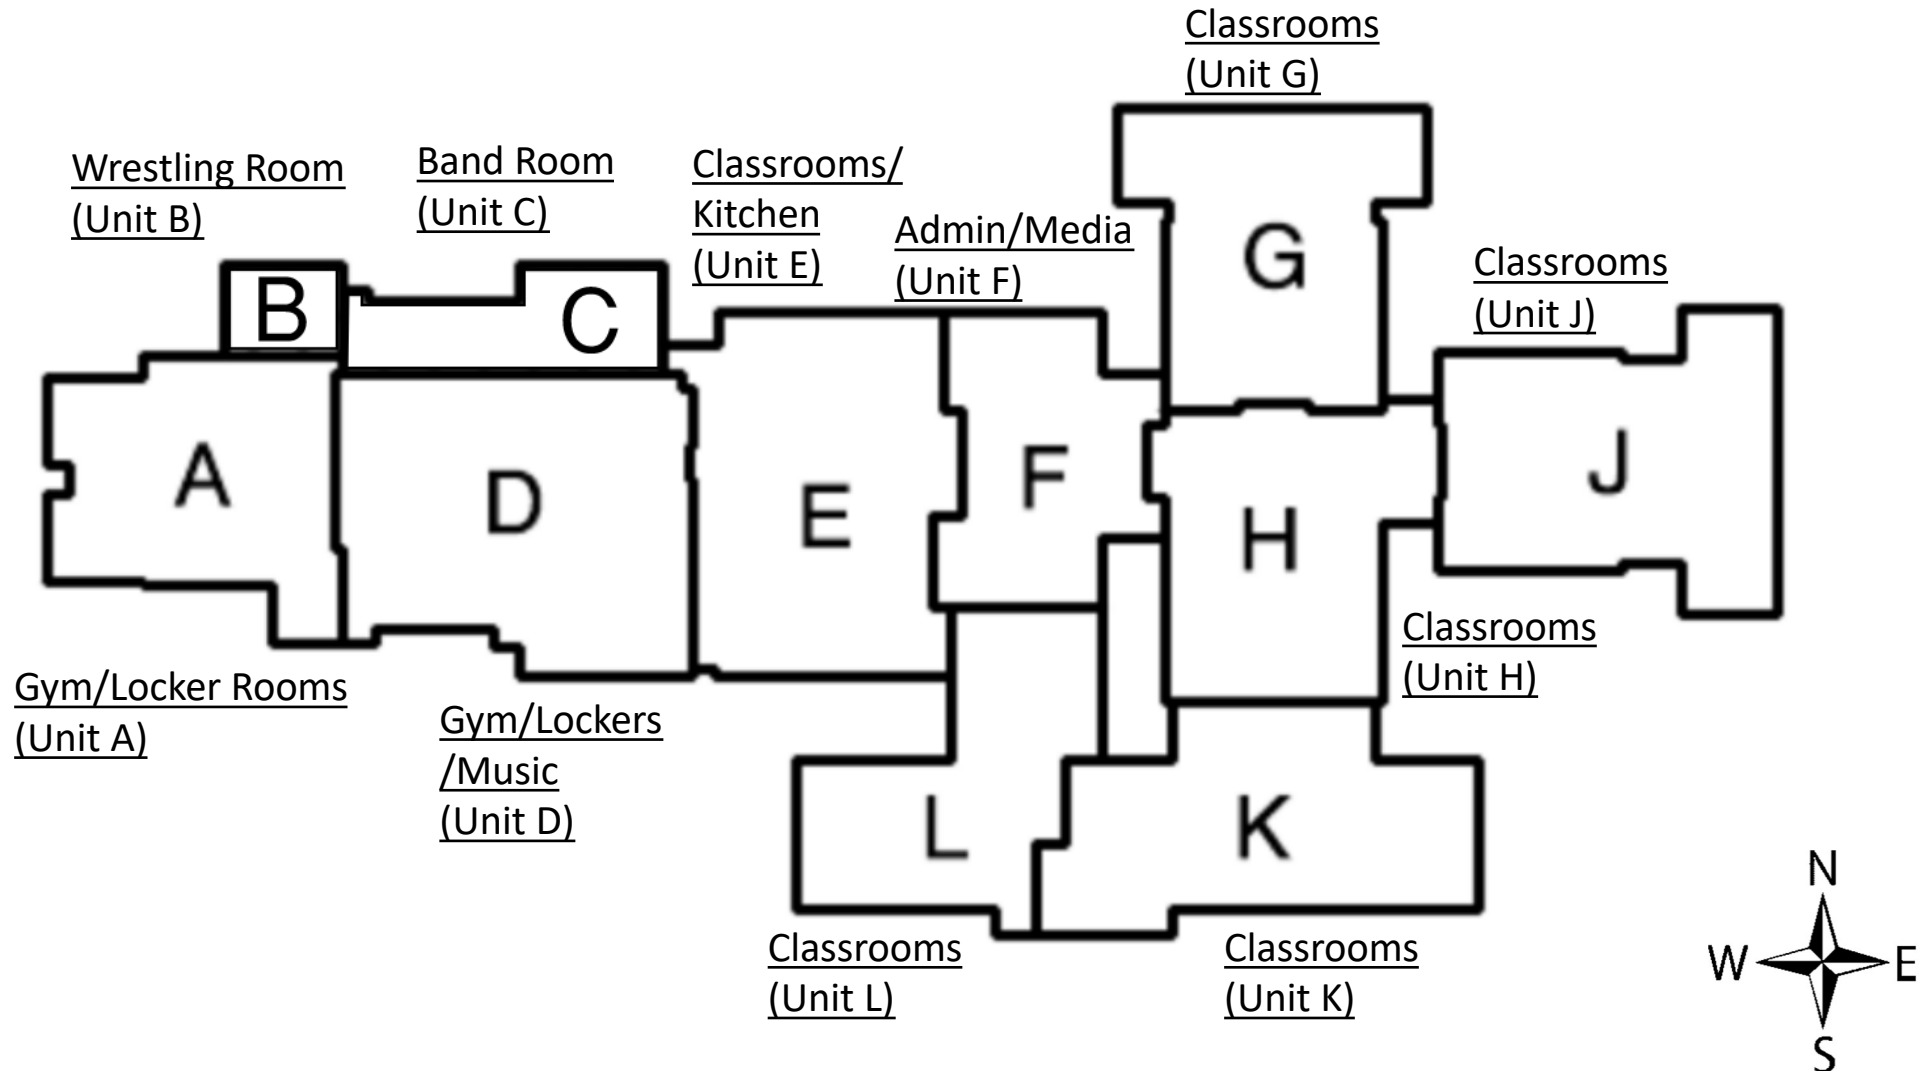




Progress Photographs



Westchester Intermediate

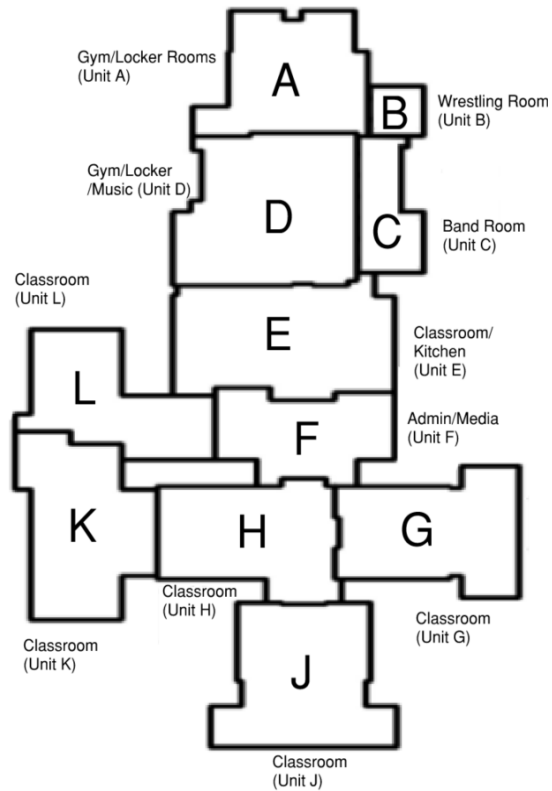

**Board Update
March 6, 2023**




Aerial View



Progress Photographs



Westchester Intermediate

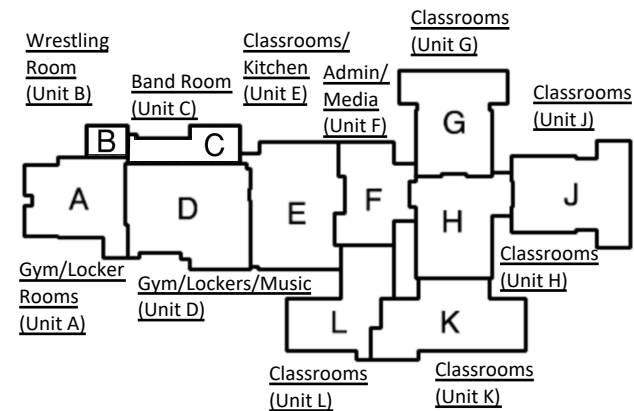

**Board Update
March 6, 2023**



Unit G Classrooms



Unit L & K Roof

Progress Last Four Weeks


- Completed structural steel in Unit A addition
- Completed concrete masonry unit wall in Unit A addition
- Began face brick for Unit K
- Completed interior metal stud walls in Units K & L
- Completed drywall in Unit F



Progress Photographs



Westchester Intermediate

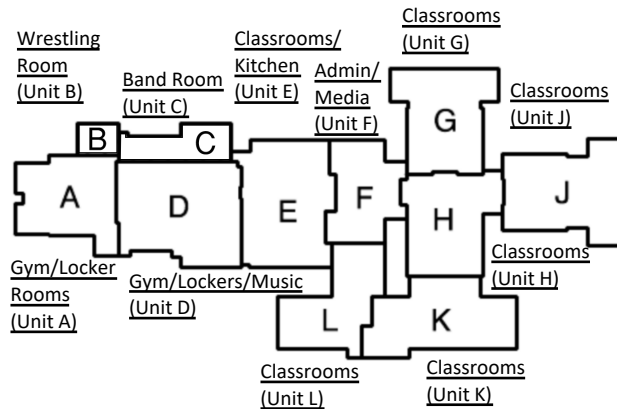

**Board Update
March 6, 2023**



Unit F Canopy Concrete




Unit G Bathroom

Next Four Weeks

- Complete mechanical, electrical, plumbing rough-in for Units K & L
- Complete hanging drywall in Units K & L
- Begin soffits and roof for Unit A locker rooms
- Complete flooring, bathroom partitions, marker boards in Unit G
- Complete exterior metal stud wall in Units G & J



Yost Elementary Key Plan

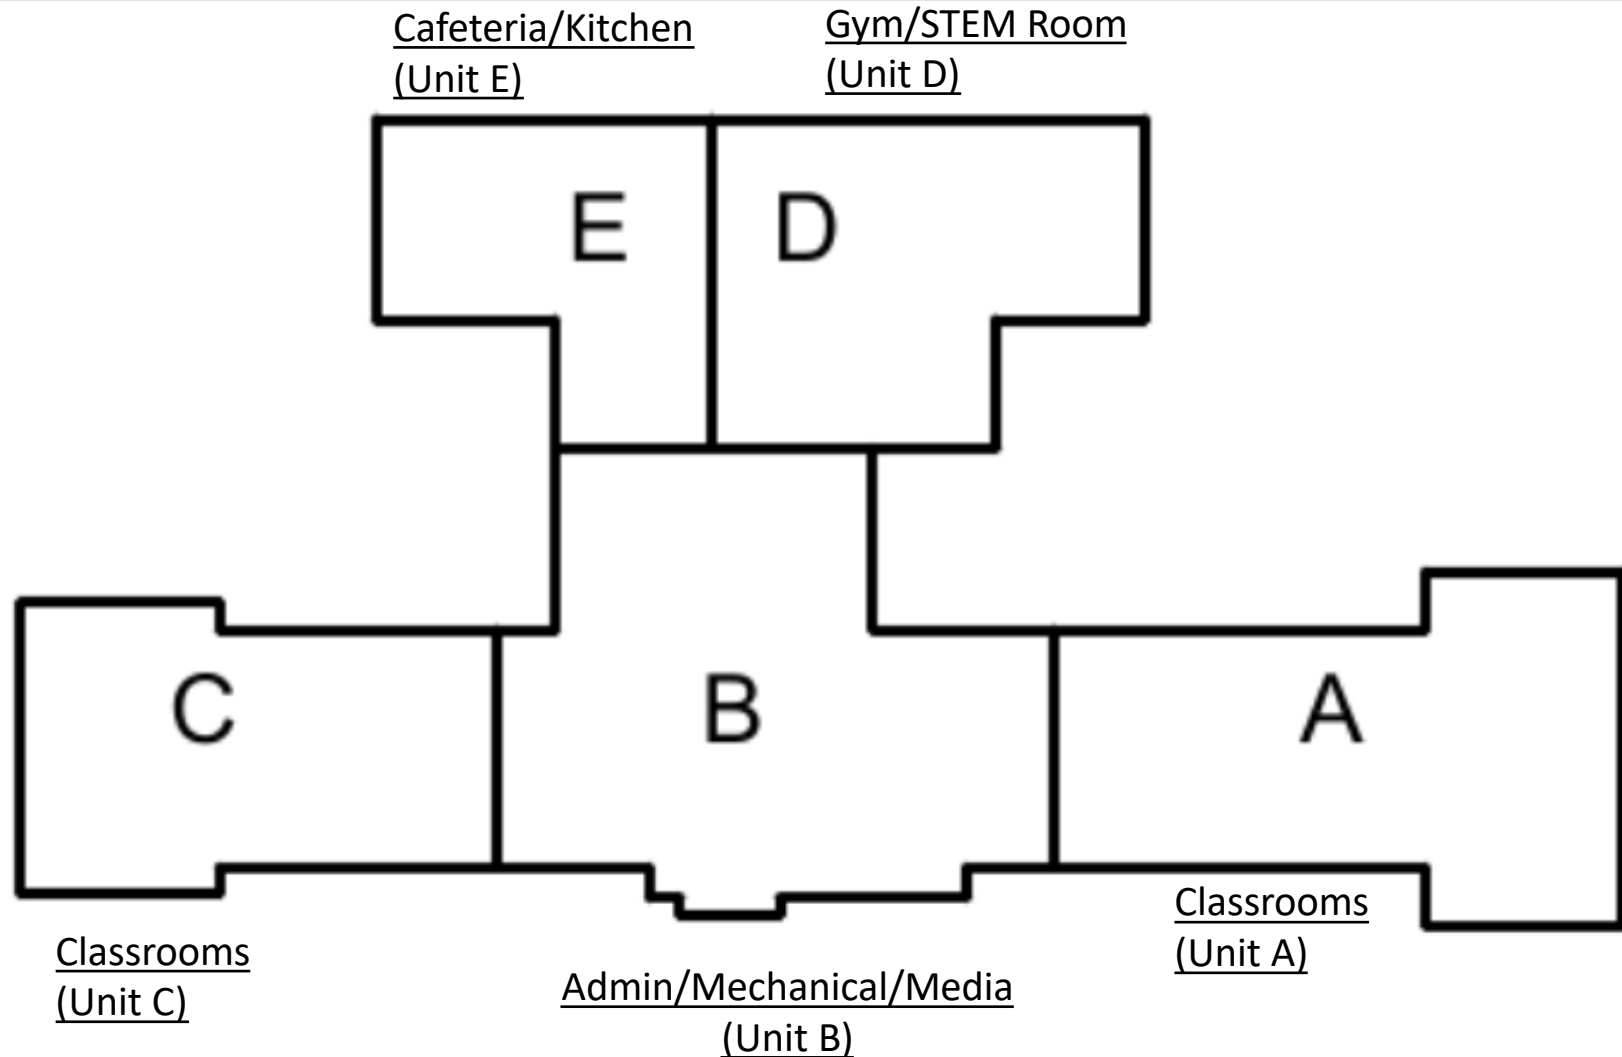





Progress Photographs



Yost Elementary

Cafeteria/Kitchen
(Unit E)

Gym/STEM Room
(Unit D)



Classrooms
(Unit C)

Admin/Mechanical/Media
(Unit B)

Classrooms
(Unit A)

**Board Update
March 6, 2023**



Aerial View




Progress Photographs



Yost Elementary

Cafeteria/Kitchen
(Unit E)

Gym/STEM Room
(Unit D)

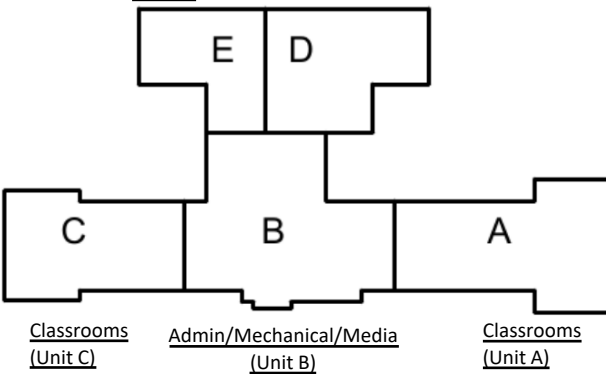

Exterior Brick



Unit B Mezzanine

Progress Last Four Weeks

- Completed roof truss installation in Units A, B, & C
- Completed steel roof deck installation in Units A, B, & C
- Completed layout of interior walls in Unit C
- Completed slab on grade in Units A, B, & C
- Completed Unit B mezzanine roof
- Completed in-wall plumbing rough-ins in Units A & C

Board Update
March 6, 2023




Progress Photographs



Yost Elementary

Cafeteria/Kitchen
(Unit E)

Gym/STEM Room
(Unit D)

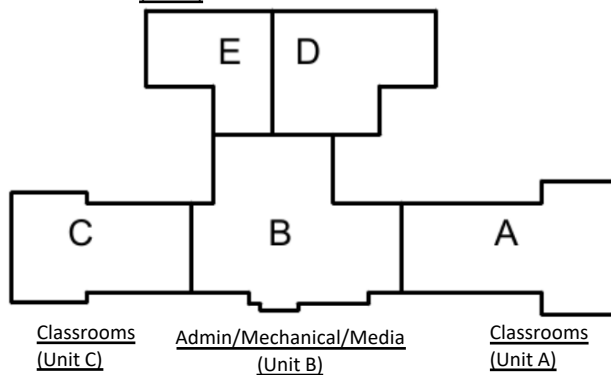

Classrooms
(Unit C)

Admin/Mechanical/Media
(Unit B)

Classrooms
(Unit A)

**Board Update
March 6, 2023**



Unit B Canopy




Main Corridor

Next Four Weeks

- Begin drywall in Unit A
- Finish framing Units B & C
- Begin Unit C roofing, ice and water shield
- Begin ductwork in the corridors
- Begin domestic water mains in the corridors
- Begin HVAC chilled and heating lines in the corridors
- Begin interior ground face block at classroom entrances



Liberty Intermediate/Middle Key Plan

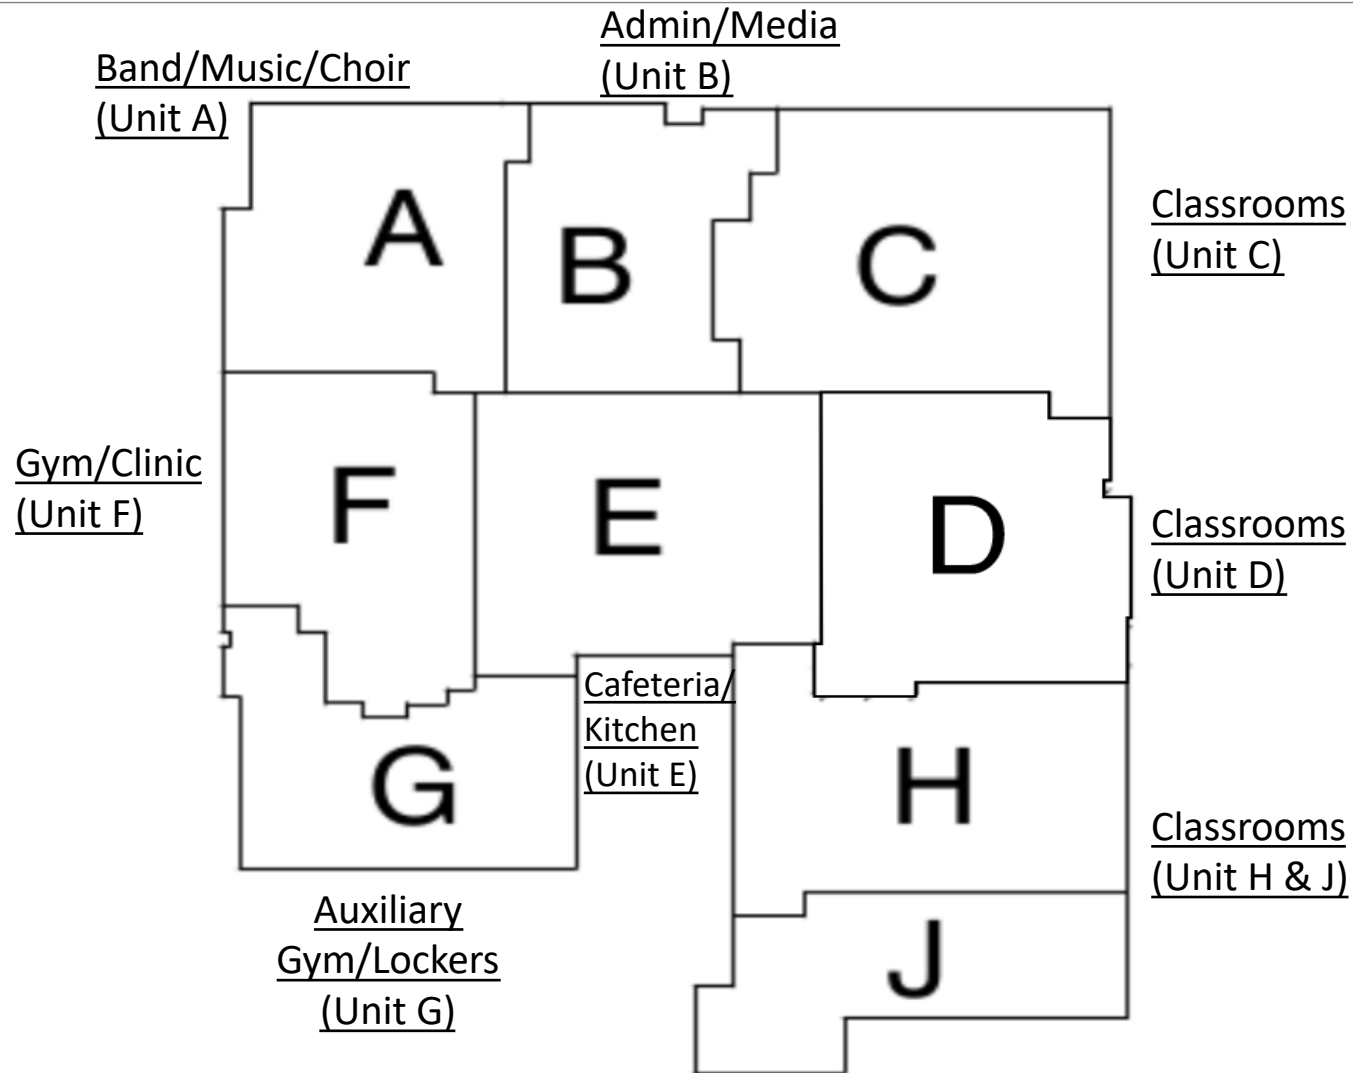




Progress Photographs



Liberty Intermediate

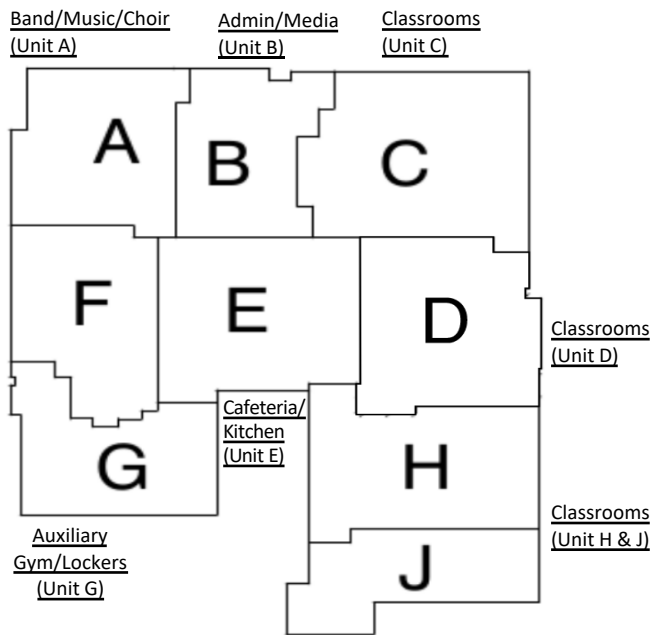

Board Update
March 6, 2023


Aerial View



Progress Photographs



Liberty Intermediate

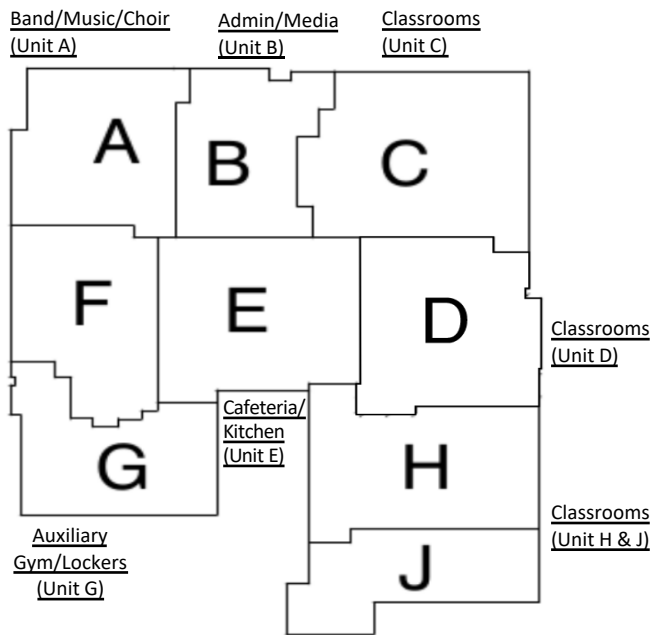

**Board Update
March 6, 2023**



Progress Last Four Weeks


- Completed installing casework in Unit B Admin Area & Media Center
- Completed installing wall covering in Unit C.1 classrooms
- Completed resinous flooring in Unit B restrooms
- Completed hard tile in Unit B restrooms
- Completed ceiling and light fixtures in Units B & C




Progress Photographs



Liberty Intermediate

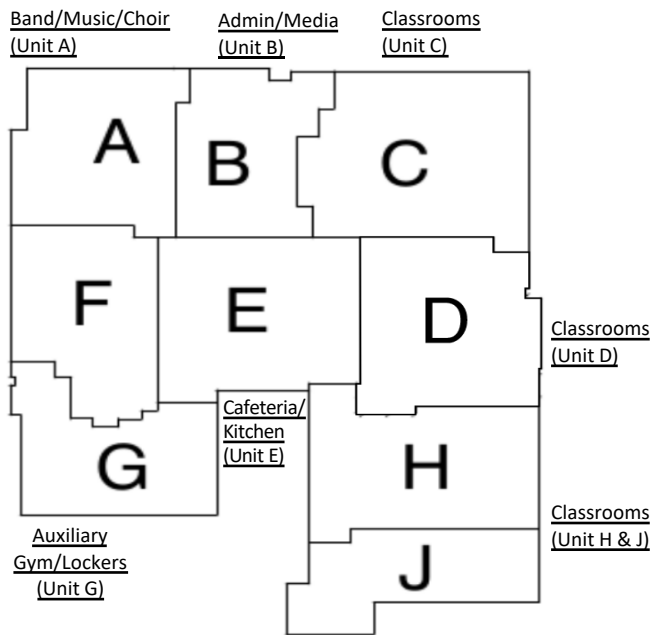

**Board Update
March 6, 2023**

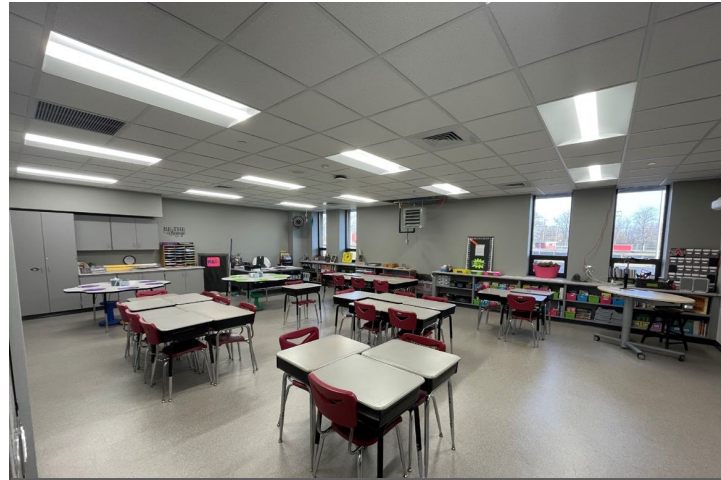

Unit C Classrooms



Unit B Main Entrance

Next Four Weeks

- Begin demo in Unit A music and band
- Begin demo in Unit C.2 classrooms
- Complete relocation of utilities
- Begin footing and foundations for Unit H & J
- Complete framing for Unit B canopy



Questions?
